ID	Task Name	Duration	Start	Finish
1	Undergrounding of overhead utility lines	25 days	Mon 11/17/08	Fri 12/19/08
2	Commence On- Site	0 days	Mon 12/1/08	Mon 12/1/08
3	Mobilization/ Sediment control/ Site Clearing (Daily Hauling-off asphalt & debris) (26th Street Entrance)	15 days	Mon 12/1/08	Fri 12/19/08
4	Relocate site entrance to Yorktown Rd.	1 day	Fri 12/19/08	Fri 12/19/08
5	Excavations Support (Installation of soldier beams steady over initial 3 weeks) (Pile will be installed by vibratory means until refusal, then completed with Hammer)	40 days	Mon 12/22/08	Fri 2/13/09
6	Excavation (Daily Hauling- off Dirt) (26th Street Entrance initially, then Yorktown entrance)	45 days	Mon 1/19/09	Fri 3/20/09
7	Build Concrete Structure (Daily deliveries including Formwork, Reinforcing Steel, and Concrete)	6 mons	Mon 3/9/09	Fri 8/21/09
8	Precast Façade (Daily deliveries include tractor trailers with precast panels) (Yorktown Pedestrian Bridge will be installed in this timeframe)	3.5 mons	Mon 8/10/09	Fri 11/13/09
9	Window Installation (Materials will be delivered regularly) (Installation occurs from within structure)	3.5 mons	Mon 8/24/09	Fri 11/27/09
10	Roofing (Materials will be delivered regularly) (Installation occurs on site)	4 mons	Mon 8/31/09	Fri 12/18/09
11	Building Fit out (Includes all activities from framing, rough-in through paint and cabinets) (deliveries will be regular if not daily) (Trash removal will occur daily)	13.5 mons	Mon 7/13/09	Fri 7/23/10
12	New Utilities (New wet utilities to building entails trenching activities) (This involves work on Yorktown and in the public space which will impact traffic)	2 mons	Mon 7/13/09	Fri 9/4/09
13	Hardscape & Landscape (Includes lighting, walks, and trees around the perimeter of the site) (Work will impact public spaces and traffic flow)	4 mons	Mon 3/1/10	Fri 6/18/10
14	Substantial Completion of the Project - Certificate of Occupancy	1 day	Thu 7/1/10	Thu 7/1/10
15	Move Equipment and Furniture into building. (Daily delivery of material, some trash removal still occurring)	21 days	Fri 7/2/10	Fri 7/30/10
16	Final Occupancy - (Move in of students)	15 days	Mon 8/2/10	Fri 8/20/10

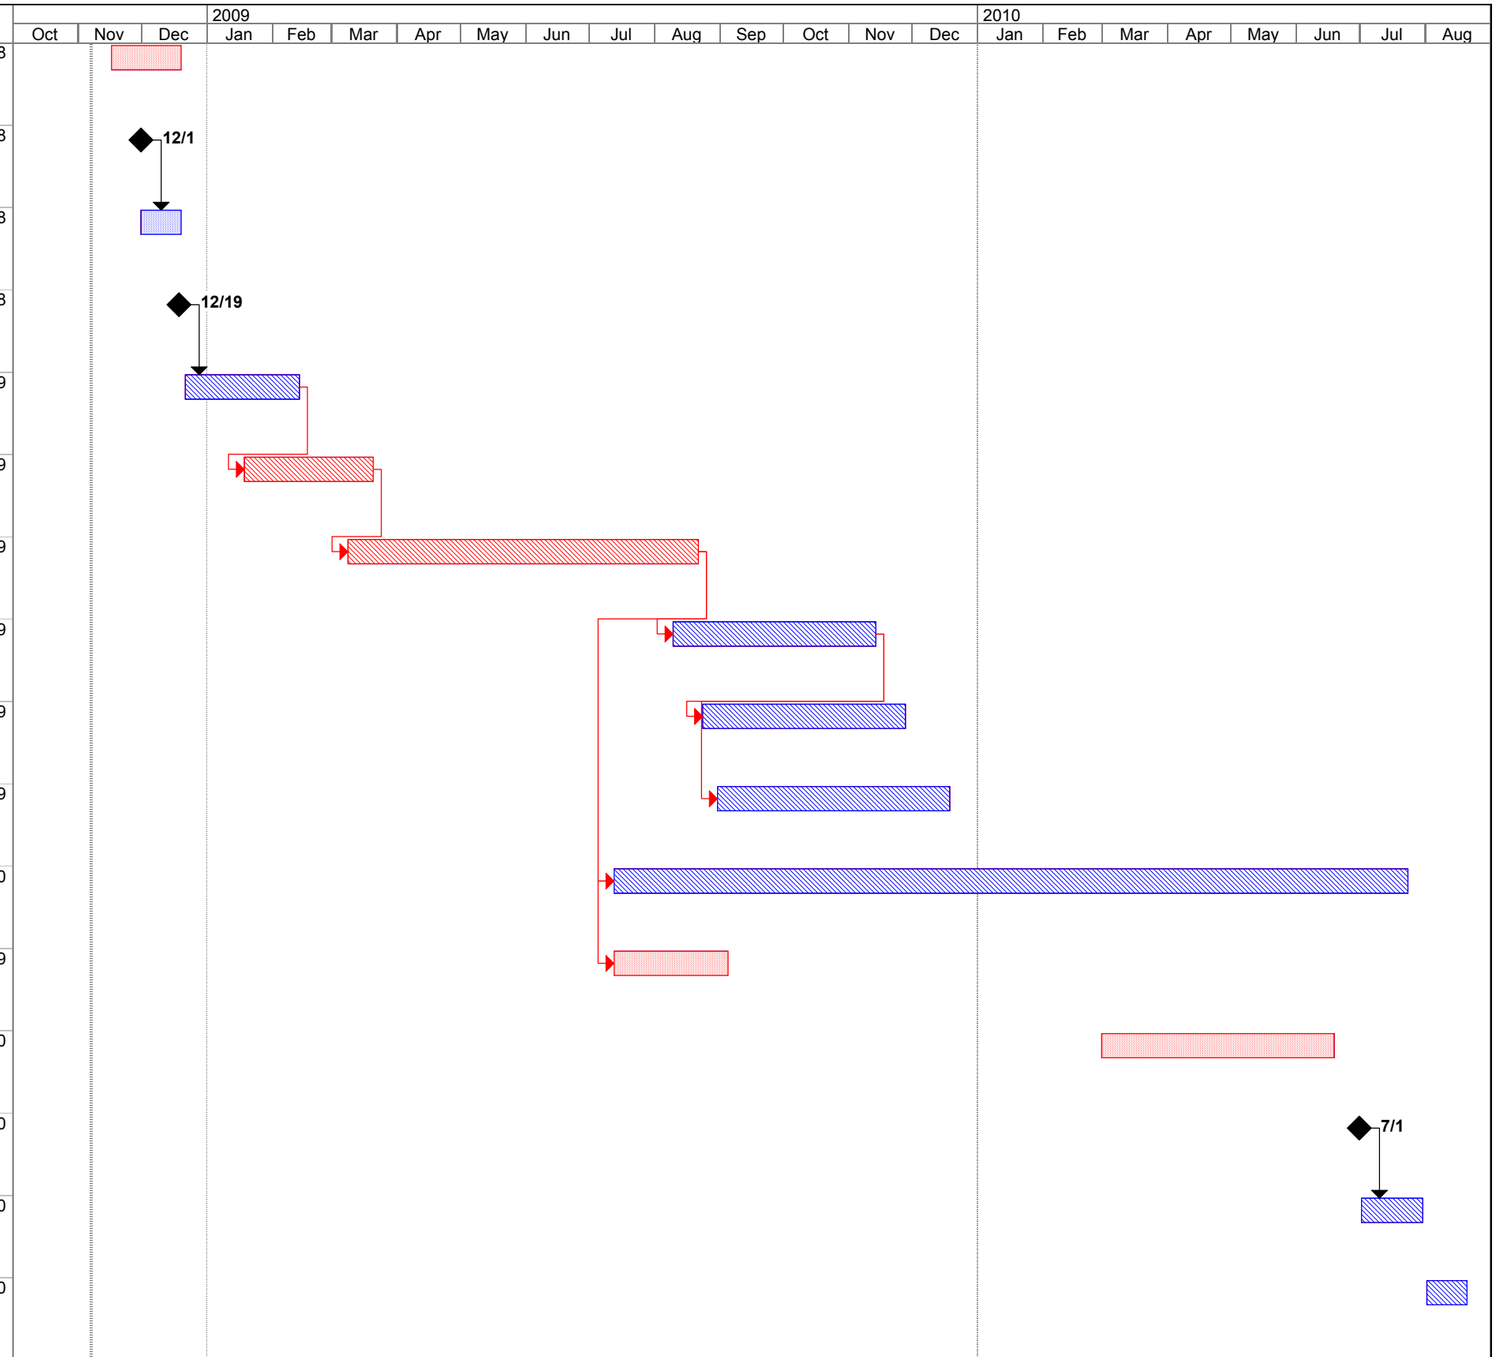

Project: Marymount NRC schedule
Date: Fri 11/7/08

High Traffic Activities	Moderate Traffic Impact	Milestone	External Tasks		
Moderate Traffic Activities	Split	Summary	External Milestone		
High Traffic Impact	Progress	Project Summary	Deadline		
